


ID	Task	Task Name	Duration	Start	Finish
1		<b>Pre-Construction</b>	<b>34 days</b>	<b>Tue 1/28/25</b>	<b>Fri 3/14/25</b>
2		Bid Invite Distribution	16 days	Tue 1/28/25	Tue 2/18/25
3		Bids Due	0 days	Tue 2/18/25	Tue 2/18/25
4		Post Bids	3 days		Fri 2/21/25
5		WMH CoC Issue LOI	0 days	Fri 2/21/25	Fri 2/21/25
6		Long Lead Submittals	15 days		Fri 3/14/25
7		Owner Review / Contract Award	15 days		Fri 3/14/25
8		<b>Construction</b>	<b>205 days</b>	<b>Fri 3/14/25</b>	<b>Fri 12/26/25</b>
9		Precast Procurement	100 days		Fri 8/1/25
10		Structural Steel Procurement	70 days		Fri 6/20/25
11		Mechanical Procurement	130 days		Fri 9/12/25
12		Electrical Procurement	150 days		Fri 10/10/25
13		<b>Project Commencement</b>	<b>0 days</b>	<b>Fri 3/14/25</b>	<b>Fri 3/14/25</b>
14		Demolition	10 days		Fri 5/9/25
15		Infill Existing Building Openings	2 days		Tue 4/29/25
16		<b>GROUNDBREAKING</b>	<b>0 days</b>	<b>Mon 5/5/25</b>	<b>Mon 5/5/25</b>
17			10 days		Fri 5/23/25
18		Footings / Foundations	10 days		Fri 6/6/25
19		Stair Tower / Elevator Shaft	10 days	Mon 6/9/25	Fri 6/20/25
20		Structural Steel Frame / Decking	15 days		Fri 7/11/25
21		Slab on Metal Deck	5 days		Fri 7/18/25
22		2nd Floor Framing	10 days		Fri 8/1/25
23		2nd Floor MEP R/I	10 days	Mon 8/4/25	Fri 8/15/25
24		Set Rooftop MEP Equipment	5 days		Fri 9/19/25
25		Precast Erection	15 days	Mon 8/4/25	Fri 8/22/25
26		Main Roof Installation	5 days		Fri 8/29/25
27		Window / Door Installation	10 days	Mon 9/1/25	Fri 9/12/25
28		Exterior Canopies	10 days	Mon 9/1/25	Fri 9/12/25
29		<b>Building Enclosure</b>	<b>0 days</b>	<b>Fri 9/12/25</b>	<b>Fri 9/12/25</b>
30			5 days		Fri 8/29/25
31		Underground MEP	10 days	Mon 9/1/25	Fri 9/12/25
32		Vapor Mitigation System	5 days	Mon 9/8/25	Fri 9/12/25
33		Slab on Grade	5 days		Fri 9/19/25
34		1st Floor Framing	10 days		Fri 10/3/25
35		1st Floor MEP R/I	10 days		Fri 10/17/25
36		2nd Floor Concrete Polishing	5 days		Fri 8/22/25
37		2nd Floor Drywall	10 days		Fri 9/26/25
38		2nd Floor Interior Finishes	25 days		Fri 10/31/25
39		1st Floor Concrete Polishing	5 days		Fri 10/24/25
40		1st Floor Drywall	10 days		Fri 11/7/25
41		1st Floor Interior Finishes	25 days		Fri 12/12/25
42		Elevator Installation	20 days		Fri 10/10/25
43		Site Work	15 days		Fri 10/3/25
44		Landscaping / Specialties	20 days		Fri 10/31/25
45		Punchlist / Owner Training	10 days		Fri 12/26/25
46		Project Turnover	0 days	Fri 12/26/25	Fri 12/26/25

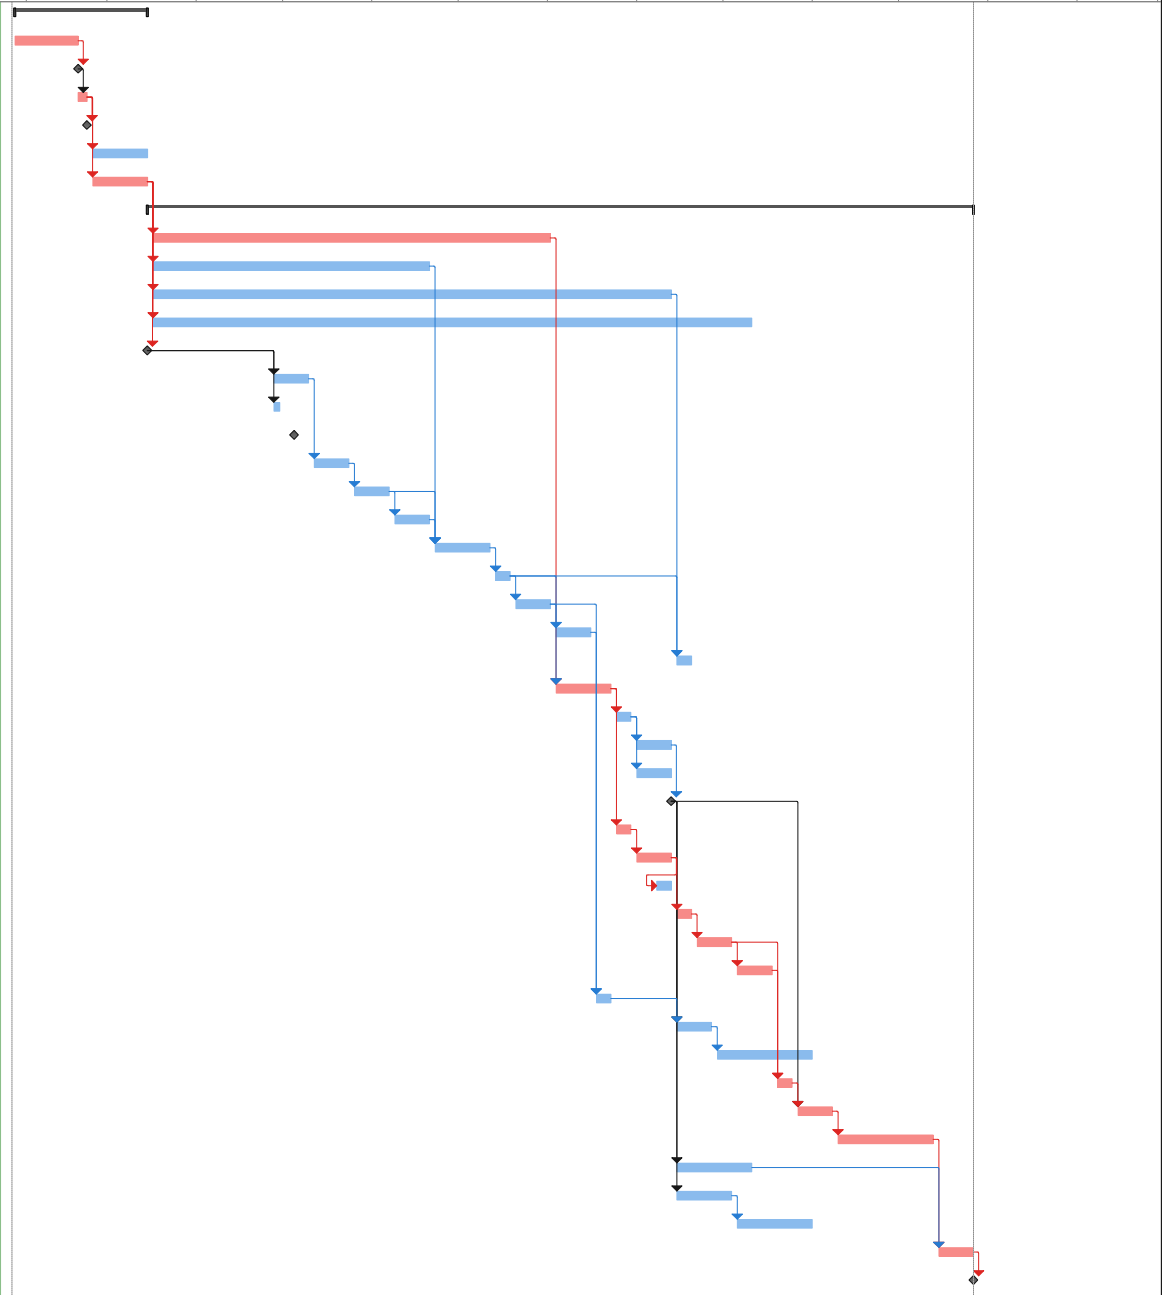

Project: WMH CoC DRAFT SCH  
Date: Thu 1/23/25

Task Split	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Milestone	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress
